Additional fund for R.K.Hegade nagara Samudaya Bhavan to extend compound and grills

First and Final Bill

Key Map

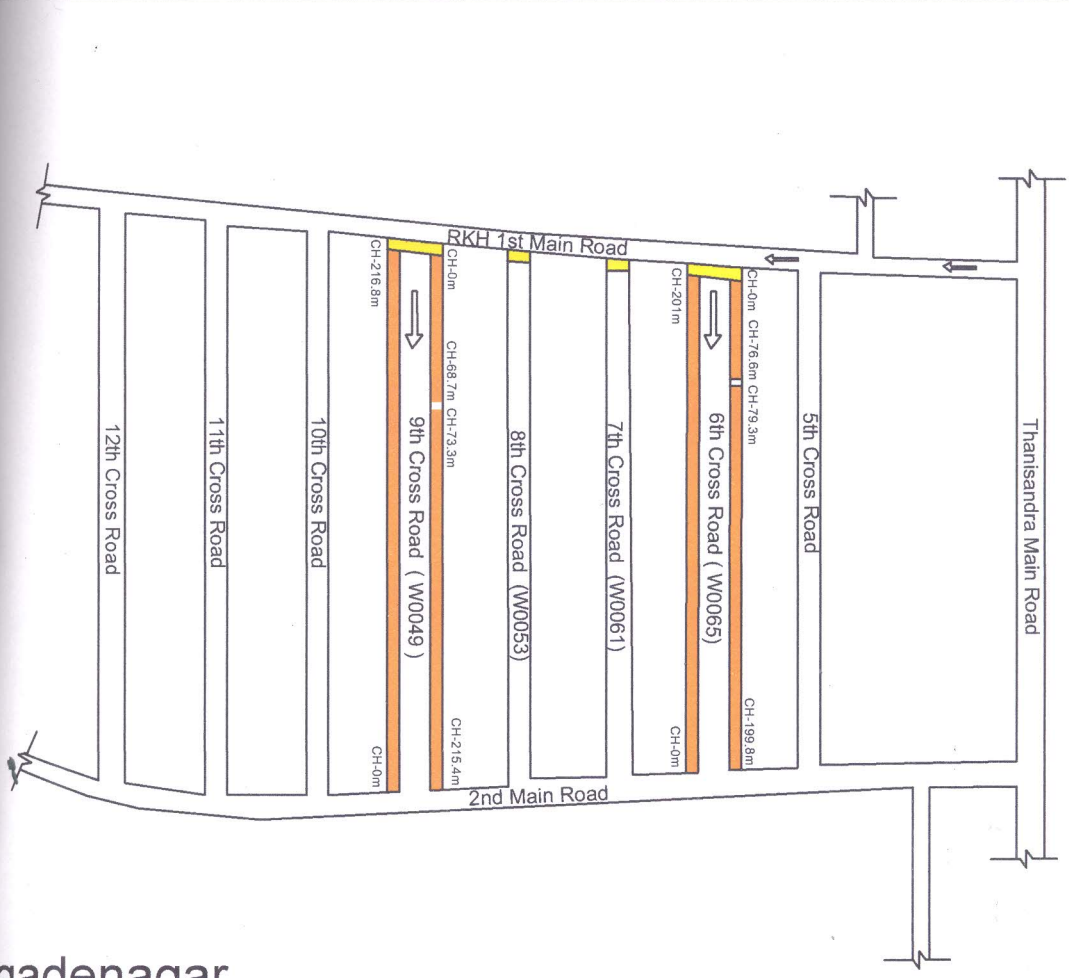

legadenagar

NOTES:-

1) Do Not Scale The Drawings
2) All Dimensions Are In meters

INDEX

Flagging course with CC Cover slab & kerb

Culvert

PROJECT	Additional fund for R.K.Hegade nagara Samudaya Bhavan to extend compound and grills
CLIENT	BBMP

RUDRAPRASAD CONSULTANTS
STRUCTURAL ENGINEERS, ARCHITECTS
& PROJECT MANAGEMENT CONSULTANTS
No. 3 7th MAIN,
MALLESWARAM BANGALORE-560003
Ph : 23444801
Mob : 91-9448227083,91-9972924526
E-mail: rudraprasad3@rediffmail.com
Web: www.arkengineers.com

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

BRUHAT BENGALURU

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Additional Fund for R.K.Hegade Nagara Samu
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	9-Mar-21
	Project End Date	:	7-Jul-21
	Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Tender Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*
1	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an average lift upto 0.5 m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods	Cum	685.59	911.33	100	10-03-21	19-04-21
2	Removing and refixing stone slabs of drains and pointing in CM (1:3) and as per the directions of the Engineer in charge	Sqm	850.50	849.96	100	20-03-21	19-04-21
3	Providing granite slabs of selected quantity roughly dressed and fixed in cement mortar (1:6) including fixing curing etc.and as per the directions of the Engineer in charge	Sqm	364.50	365.72	100	25-03-21	19-04-21
4	Providing and laying Plain cement concrete of mix 1:3:6 with OPC @ 20kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.84cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing	Cum	175.39	175.10	100	31-05-21	30-06-21

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

J MAHANAGARA PALIKE

laya Bhavana to Extend Compound and Grills.

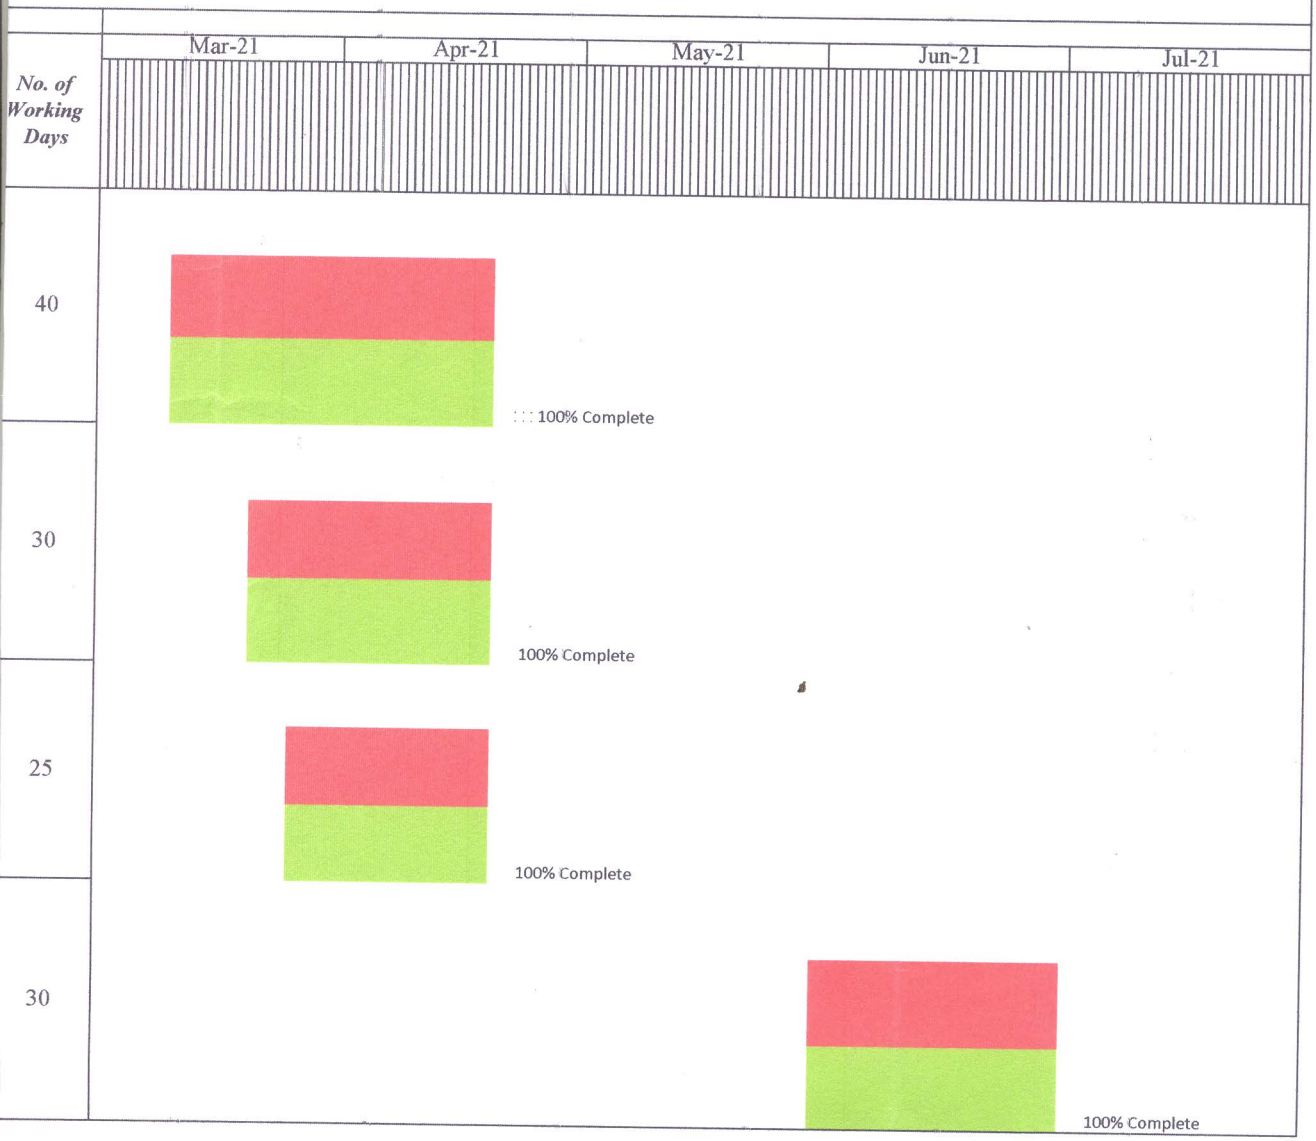

ಪಾಲಿಕೆ ಅಭಿಯಂತರರು
ನಮರ ಉಪ ವಿಭಾಗ
ಟಿ., ಬೆಂಗಳೂರು-24

RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Additional Fund for R.K.Hegade Nagara Samud
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	9-Mar-21
	Project End Date	:	7-Jul-21
	Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Tender Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*
5	Providing and constructing granite / trap / basalt size stone masonry in basement with cement mortar 1:6, edges of stones chistle dressed in courses not less than 15 cms high, bond stones at two m. apart in each course including cost of materials, labour, curing complete as per specifications and as per the directions	Cum	34.56	34.76	100	27-05-21	02-06-21
6	Providing and constructing load bearing wall with solid concrete blocks having block density not less than 800 kg/m3 having a minimum average compressive strength 4.00 N/mm2 confirming to IS 2185 (Part) : 2005and constructed with CM 1:4 , as per IS 2572:2005 including	Sqm	1080.00	1080.36	100	31-05-21	30-06-21
7	Plain /Reinforcement Cement Concrete M20 with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.46cum, with superplastisiser @3lts confirming to IS9103-1999 Reaffirmed-2008,	Cum	77.22	76.62	99	03-06-21	13-06-21
8	Providing flush pointing to course stone masonry with cement mortar 1:3, 20mm deep, after raking joints to depth of 20mm nicely lining, including cost of materials, labour, curing complete as per specifications. and as per the directions of the Engineer in charge	Sqm	43.20	45.60	106	28-05-21	03-06-21

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

MAHANAGARA PALIKE

ya Bhavana to Extend Compound and Grills.

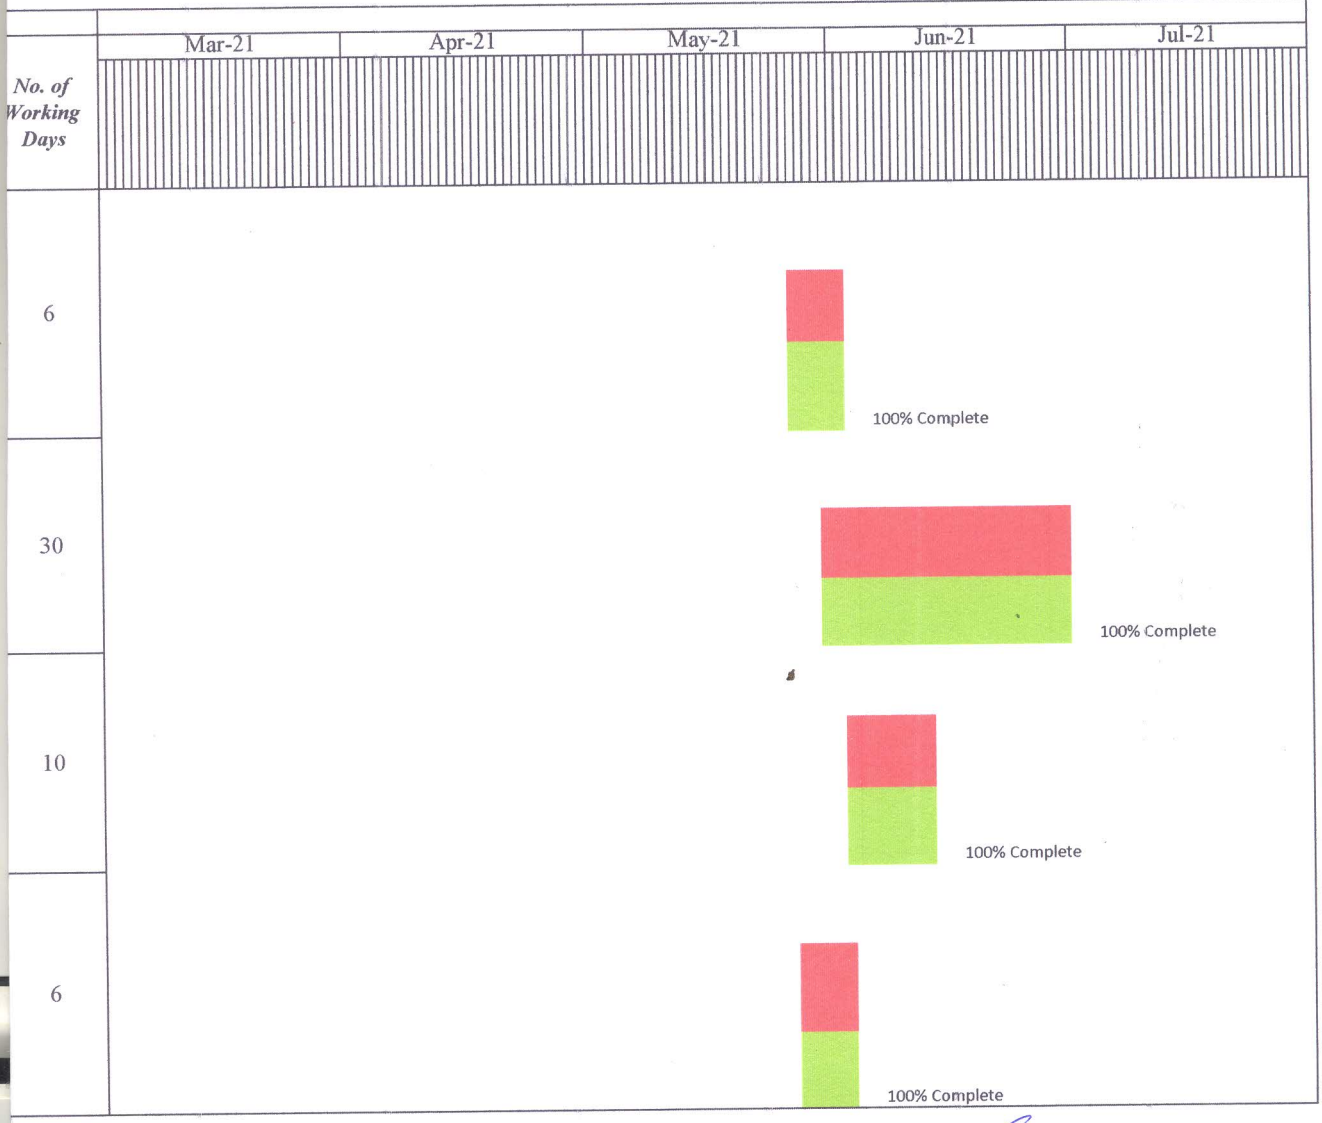

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಮಹದೇವಪುರ ವಿಭಾಗ
ಬಿ., ಬೆಂಗಳೂರು-24

RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Additional Fund for R.K.Hegade Nagara Samuc
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	9-Mar-21
	Project End Date	:	7-Jul-21
	Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Tender Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*
9	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery,	Nos	2000.00	1999.00	100	31-05-21	30-06-21
10	Applying priming coat over new wood surface and / or wood based surface after preparing the surface after throughly cleaning oil, grease, dirt and foreign matter, sand papering and knotting ready mix paint including cost of materials, labour, complete as per specifications. and as per the directions of the Engineer in charge	Sqm	270.00	269.85	100	03-06-21	29-06-21
11	Providing and applying painting two coats (excluding priming coat) on new wood surface and / or wood based surface with enamel paint to give an even shade, cleaning the surface of all dirt, dust and foreign matter, sand	Sqm	270.00	269.85	100	04-06-21	30-06-21
12	Providing and fixing RCC Precast cover slab of 100mm thick for drain in cement concrete 1:1.5:3 using graded granite jelly 20mm and down size with steel reinforcement, including form work, lift charges, curing and concrete finishing	Sqm	883.8	883.2	100	05-06-21	01-07-21
13	Providing and fixing RCC Precast cover slab of 250mm thick for drain in CC 1:2:4 using graded granite jelly 20mm and down size with steel reinforcement, including form work, lift charges, curing and concrete finishing surfaces on both	Sqm	54	57	100	05-06-21	01-07-21

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯ
ಬ್ಯಾಟರಾಯ
ಬಿ.ಬಿ.ಎಂ

MAHANAGARA PALIKE

aya Bhavana to Extend Compound and Grills.

	Mar-21	Apr-21	May-21	Jun-21	Jul-21
No. of Working Days					
30					100% Complete
26					100% Complete
26					100% Complete
26					100% Complete
26					100% Complete

ಸಹಾಯಕ ಅಧೀಕ್ಷಕ ಅಭಿಯಂತರರು
ನಗರ ಉಪ ವಿಭಾಗ
ಪೀ., ಬೆಂಗಳೂರು-24

RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Additional Fund for R.K.Hegade Nagara Samuda
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	9-Mar-21
	Project End Date	:	7-Jul-21
	Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Tender Qty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	
14	Providing and fixing M.S.Grill over existing compound wall as per using 16mm x 16mm M.S . Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S. flat for ornamental design and providing	Sqm	75.69	75.72	100	10-06-21	01-07-21	2
15	Providing and applying enamel metal paint two coats (excluding priming coat) over new steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost of	Sqm	151.38	151.44	100	12-06-21	02-07-21	2
16	Supplying and fixing M.S. Rectangular poles made out of 2 equal angles of 65x65x6 mm welded together and fixed in CC (1:2:4) WITH 2 NOS 16mm dia M.S. hold fast rods each of length 25 cms. Including cost of all materials cutting,	m	28.8	29.15	100	08-06-21	28-06-21	2
17	Providing and fixing M.S. Block pipe of 38mm dia, of heavy guage of 14 including removing the bends, cutting the pipe, and fixing pipe in between the existing two verticle poles (M.S. rectangular poles) and spot welding the	m	120	121.8	100	08-06-21	28-06-21	2
18	Providing chain link fencing 50mm size of 8 guage properly stretched between existing rectangular poles and fixed with suitable bolts & nuts, the free ends shall be welded to the pole and block pipe at top and bottom as required including	Sqm	72	70.76	98	09-06-21	04-07-21	2
19	Loading and Unloading of Stone Boulders by Manual Means complete as per specifications. and as per the directions of the Engineer in charge	Cum	1400	1294.73	92	20-03-21	29-04-21	4

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾ
ಬ್ಯಾಟರಾಯನಪು
ಬಿ.ಬಿ.ಎಂ.ಪಿ.

MAHANAGARA PALIKE

a Bhavana to Extend Compound and Grills.

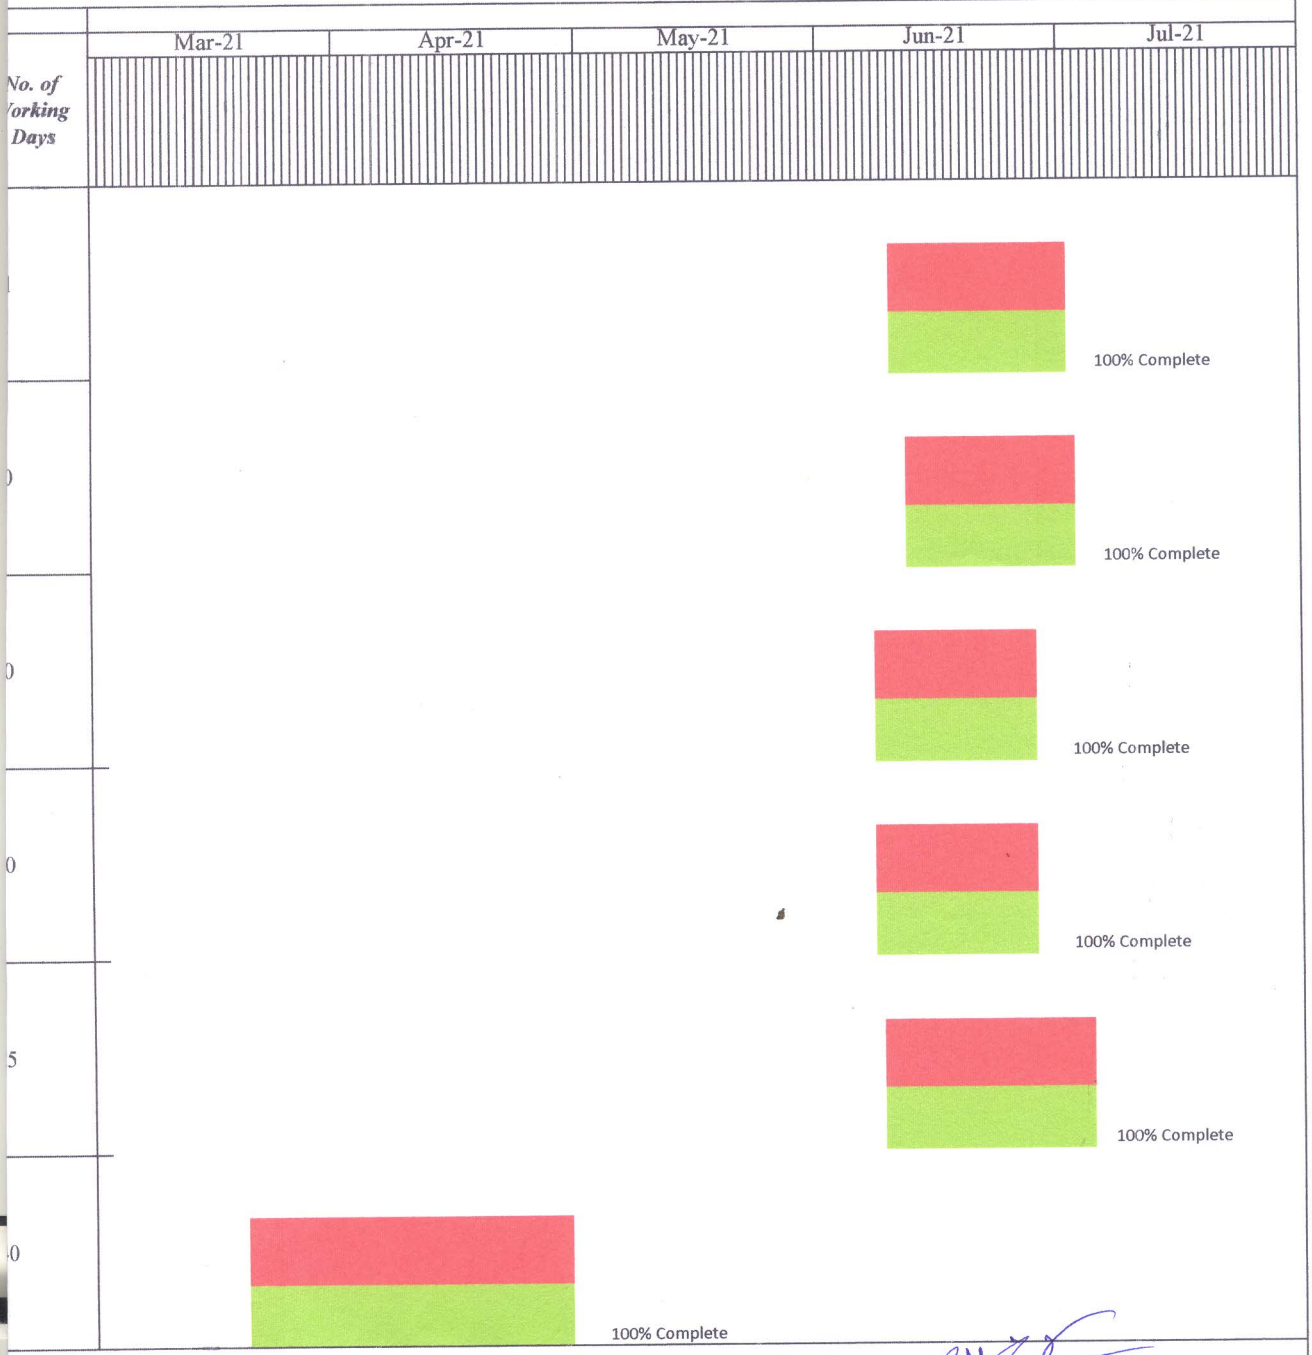

RUDRAPRASAD CONSULTANTS
BANGALORE
